


A5 bid programme - Gantt - ADD-03 [CANDIDATE - NOT VALIDATED] - planning date 2026-11-18 (PROPOSAL, not reviewed)

Earliest dates: forward pass from 2026-11-18 (first Working Day on or after the planning date, the ADD-03 [CANDIDATE - NOT VALIDATED] issue date). Latest dates: backward pass from the pack deadlines. Working Days Sun-Thu (VOL-I 2.4). Every duration, effort, waiting party and capacity is a PROVISIONAL ASSUMPTION (config/assumptions.yaml).

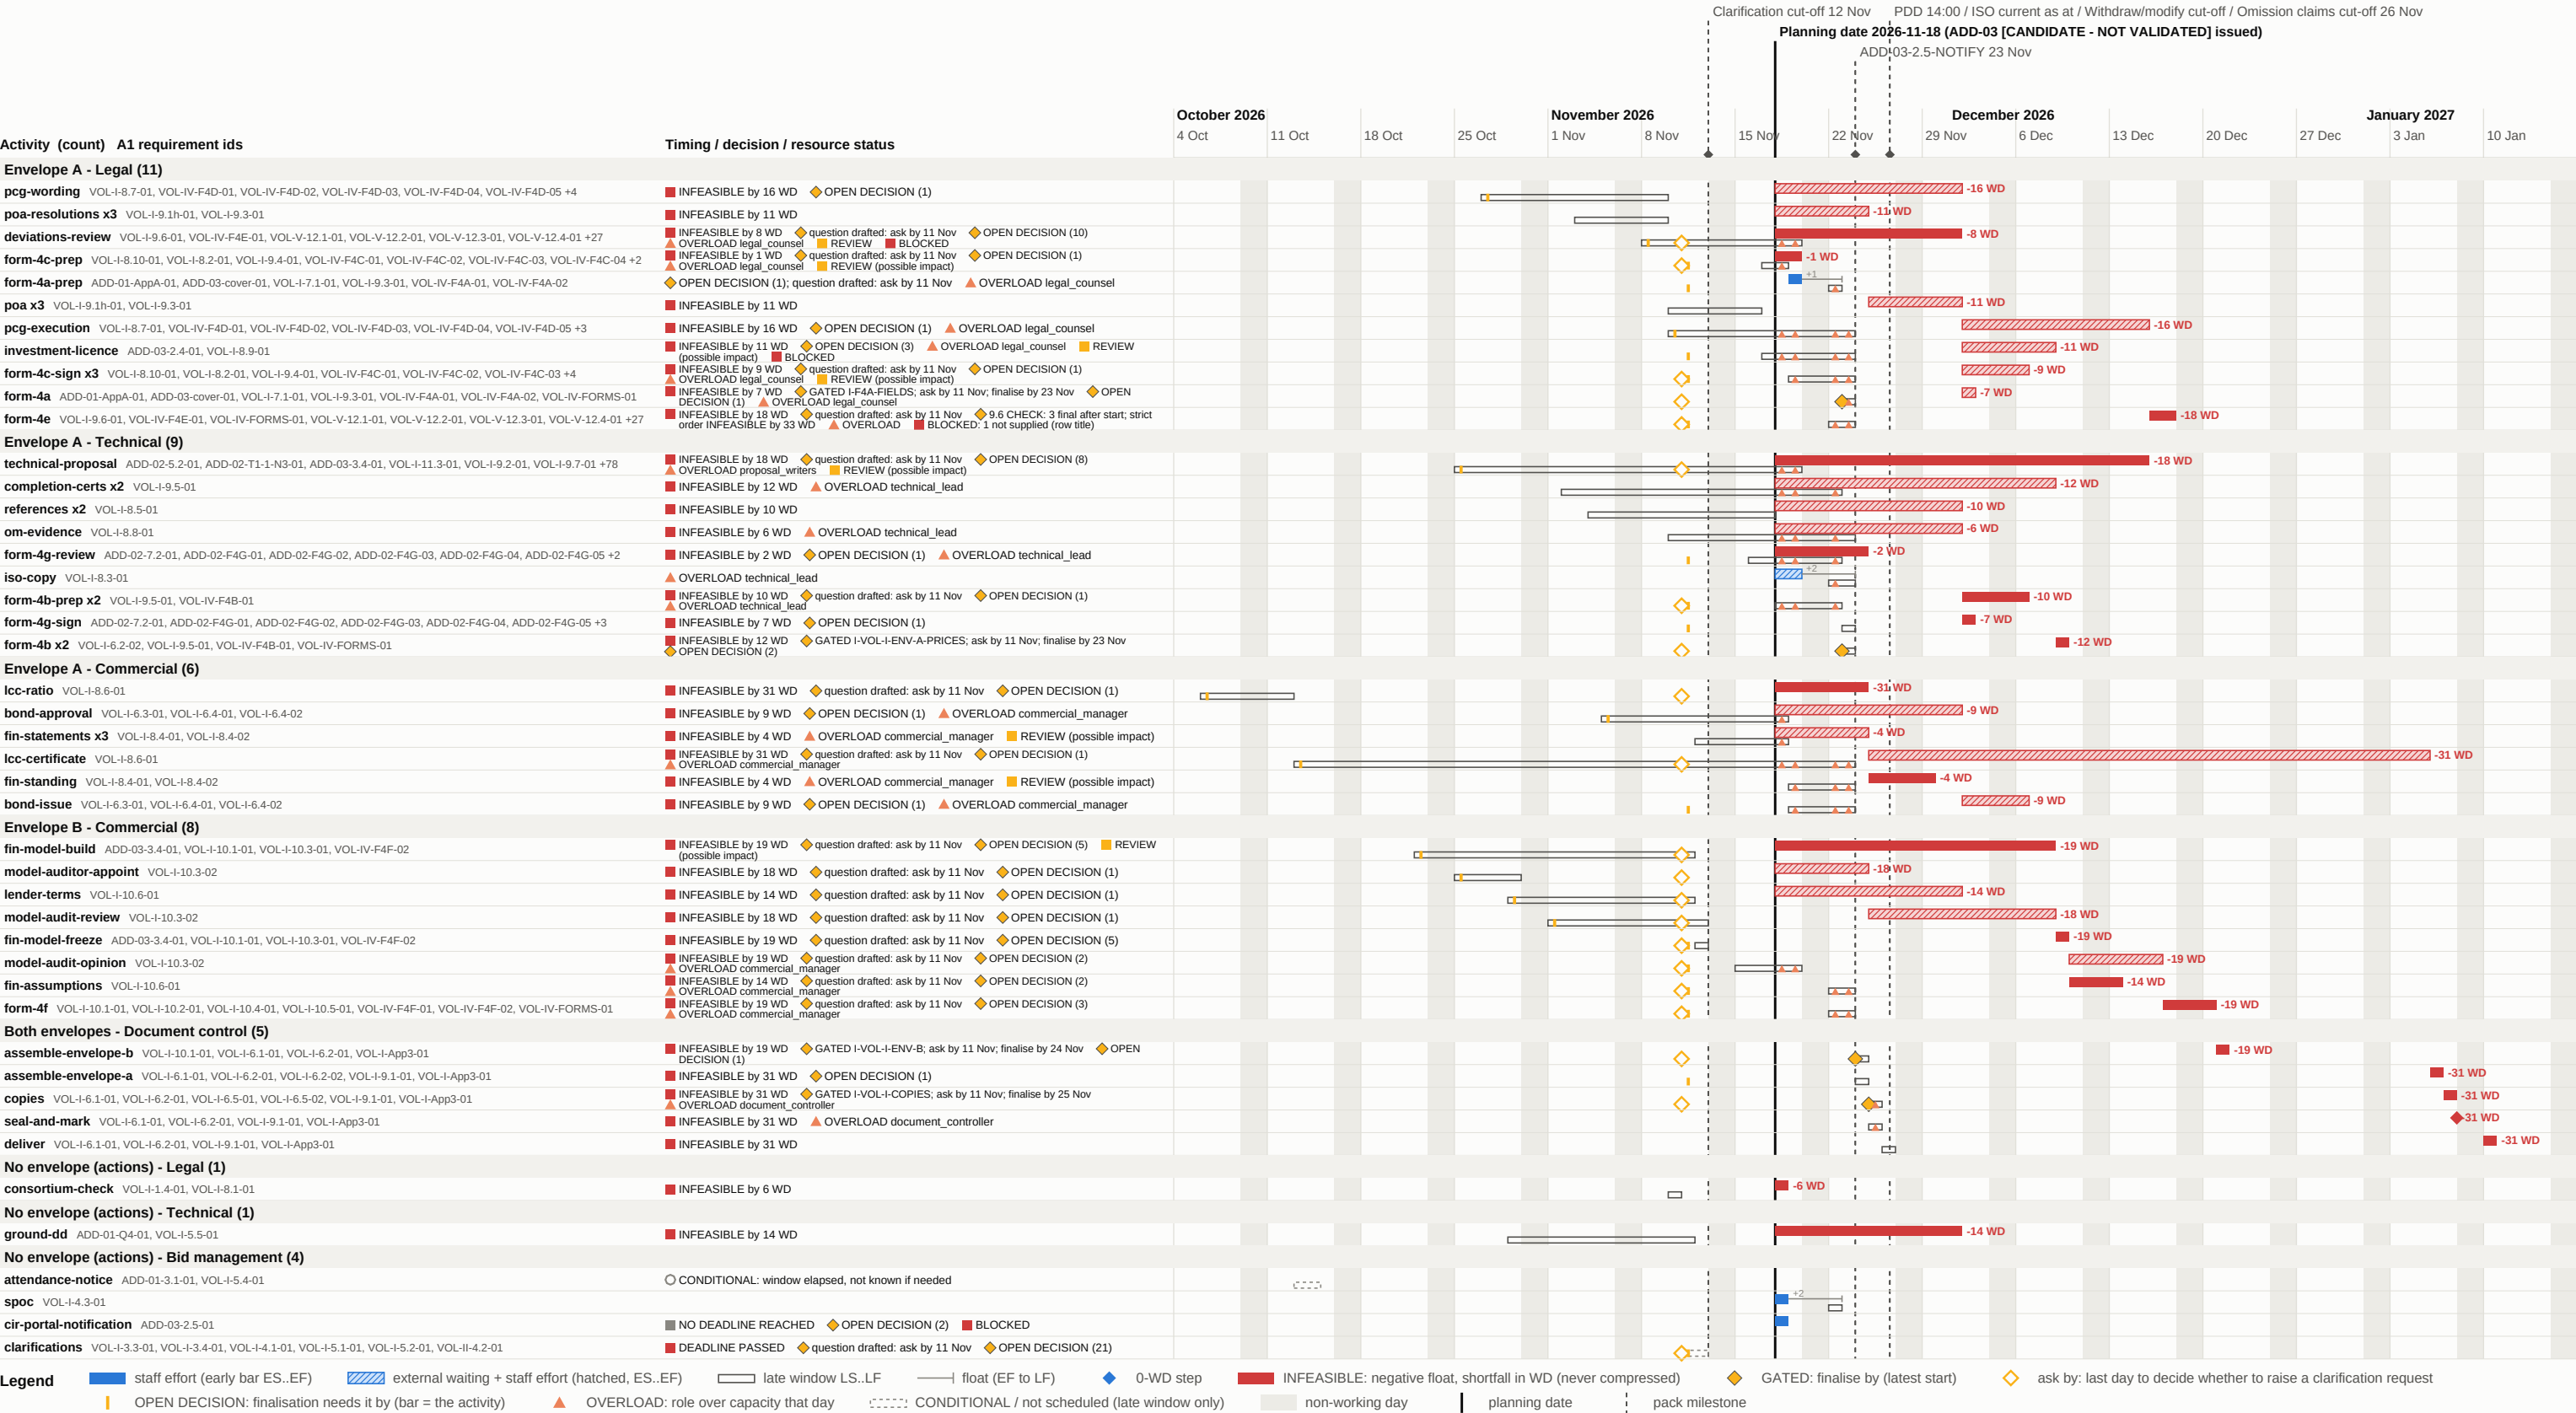

PROPOSAL, not reviewed. Timing, decision readiness and resource feasibility are separate statuses; resource levelling is NOT implemented; overloads are reported, not resolved. No bidder references, certificates, attendance or financial standing are assumed to exist.

Each row: activity id, count, then the A1 requirement ids that fit (+n more); ALL ids are in the row's hover title, gantt.html and programme.csv. Load window: late (LS..LF, clipped at the planning date).

Milestones outside the chart: Reference look-back start 2016-11-27 (conservative; 2016-11-26 if the boundary day counts); Blackout start 2026-09-14; Pre-Bid Conference 10:00 2026-09-30; Site visit (optional) 2026-10-01; Attendance-notice window ends (conditional) 2026-10-14 (conservative; 2026-10-15 if the ADD-01 issue day is excluded); Proposal validity end 2027-04-25 (conservative; 2027-04-24 if the PDD counts as day 1); Bid bond validity end 2027-05-25 (conservative; 2027-05-24 if the PDD counts as day 1).

REVIEW (<status> ...) tags: Relationship status: confirmed = stated in the documents (the entry quotes the cross-reference), not confirmed by a person; proposed = inferred by a curator or a model, a person decides; possible = a weaker inference.

OPEN DECISION (n) tags: open issues of the rows an activity's own work rests on, a person's decision with none recorded (HUMAN DECISION PENDING; also in the Flags column, programme.csv and README); clarifications lists all 24. On lcc-ratio, lcc-certificate: I-LCC-ISSUER (LCC issuer and lead time not stated). On fin-model-build, technical-proposal, fin-model-freeze: I-ADD03-PCOD-3.3 (Section 3.3 PCOD extension not applied; 3.4 requires it reflected); I-ADD03-DESIGN-FLOW (Which 'design flow' sizes the 6-hour reservoir volume). On fin-model-build, model-auditor-appoint, lender-terms, model-audit-review +5: I-VOL-I-ENV-B (Envelope B: auditor opinion and financing schedule vs VOL-I 10.1 'only'). On fin-model-build, deviations-review, fin-model-freeze, form-4e +3: I-FORM-4E-COMMERCIAL-QUALIFICATION (Form 4-E: a commercial qualification to VOL-V vs no commercial information in Envelope A (VOL-I 9.6, 6.2, 10.5)). On fin-model-build, technical-proposal, deviations-review, fin-model-freeze +4: I-CONCESSION (term from PCOD (VOL-I 12.1) or Effective Date (VOL-V 3.1)? ADD-02 Q7 cites VOL-I 3.2 only). On technical-proposal, deviations-review, form-4e: I-PERMIT (Environmental Permit not supplied; Permit compliance not claimed); I-VOL-II-T24-TENSIONS (Table 2-4 'all values are maxima' vs the chlorine and pH ranges); I-VOL-II-AT-ALL-TIMES ('at all times' (VOL-II 2.4) with each parameter's printed basis: proposed reading, not decided); I-VOL-II-COMPLIANCE-POINT (Table 2-4 compliance point: 'Point of Discharge', 'at outlet' or the delivery point (Drawing 03-C-114)?); I-FLOWS (dry weather flow undefined; Q11: design to the Volume II figures). On pcg-wording, pcg-execution: I-F4D-WORDING (Form 4-D: how far its wording may change (VOL-I 8.7)). On bond-approval, bond-issue: I-VOL-I-BOND-LONGSTOP (bid bond validity vs the Financial Close call (12.2 periods: settled by Q13)). On deviations-review, form-4e: I-FORM-4E-CROSS-CHECK (Form 4-E: how it is cross-checked against Proposal documents final after it starts (VOL-I 9.6)); I-VOL-V-MISSING (VOL-V extract: Schedules 7, 9, 11, 12 and Direct Agreement missing); I-VOL-V-PERSISTENT-BREACH ('second occurrence' of a persistent breach undefined). On form-4a-prep, form-4a: I-F4A-FIELDS (reissued Form 4-A: stale printed PDD, dropped fields, correction method). On form-4g-review, form-4g-sign: I-F4G-NO (Form 4-G: effect of a 'No' answer). On investment-licence, cir-portal-notification: I-ADD03-8.9-CONDITIONAL (VOL-I 8.9 replacement (ADD-03 2.1) not applied; conflicts with 2.4 exception). On cir-portal-notification: I-ADD03-COVER-2.5 (Cover says rejection for missing Certificate notification; Section 2.5 states none). On form-4b-prep, form-4b: I-VOL-I-ENV-A-PRICES (Form 4-B contract values vs no commercial information in Envelope A). On form-4c-prep, form-4c-sign: I-F4C-EXCLUSION (Form 4-C: 'exclusion' category). On investment-licence: I-ADD-03-INVLIC-EVIDENCE-SCOPE (EV-INVESTMENT-LICENCE and investment-licence activity if Clause 8.9 is replaced); I-INVREG-CONSEQUENCE (Table 8-1 rows: rejection only in 2.1; 2.1 op not promoted).

form-4e: VOL-I 9.6 CHECK (Form 4-E against the whole Proposal; form_4e_checks.csv); lcc-certificate, form-4f, model-audit-opinion final after Form 4-E starts on 2026-12-16; a strict order (Form 4-E after every Proposal document) INFEASIBLE by 33 WD on the assumed durations; 31 WD of it existed before the ordering (assemble-envelope-a, bond-approval, bond-issue, completion-certs, copies, deliver, fin-assumptions, fin-model-build, fin-model-freeze, fin-standing, fin-statements, form-4a, form-4b, form-4b-prep, form-4c-prep, form-4c-sign, form-4e, form-4f, form-4g-review, form-4g-sign, ground-dd, investment-licence, lcc-certificate, lcc-ratio, lender-terms, model-audit-opinion, model-audit-review, model-auditor-appoint, om-evidence, pcg-execution, pcg-wording, poa, poa-resolutions, references, seal-and-mark already late); the ordering itself adds 2 WD and makes late form-4a-prep. HUMAN DECISION PENDING: I-FORM-4E-CROSS-CHECK (Bid management); I-FORM-4E-COMMERCIAL-QUALIFICATION (Legal counsel); no duration, setting or dependency was changed
