CANDIDATE - proposed by the AI workflow, not reviewed or accepted by human review or tender release.

A5 bid programme - Gantt - ADD-03 [CANDIDATE - NOT VALIDATED] - planning date 2026-11-08 (PROPOSAL, not reviewed)

Earliest dates: forward pass from 2026-11-08 (first Working Day on or after the planning date, the ADD-03 [CANDIDATE - NOT VALIDATED] issue date). Latest dates: backward pass from the pack deadlines. Working Days Sun-Thu (VOL-I 2.4). Every duration, effort, waiting party and capacity is a PROVISIONAL ASSUMPTION (config/assumptions.yaml).

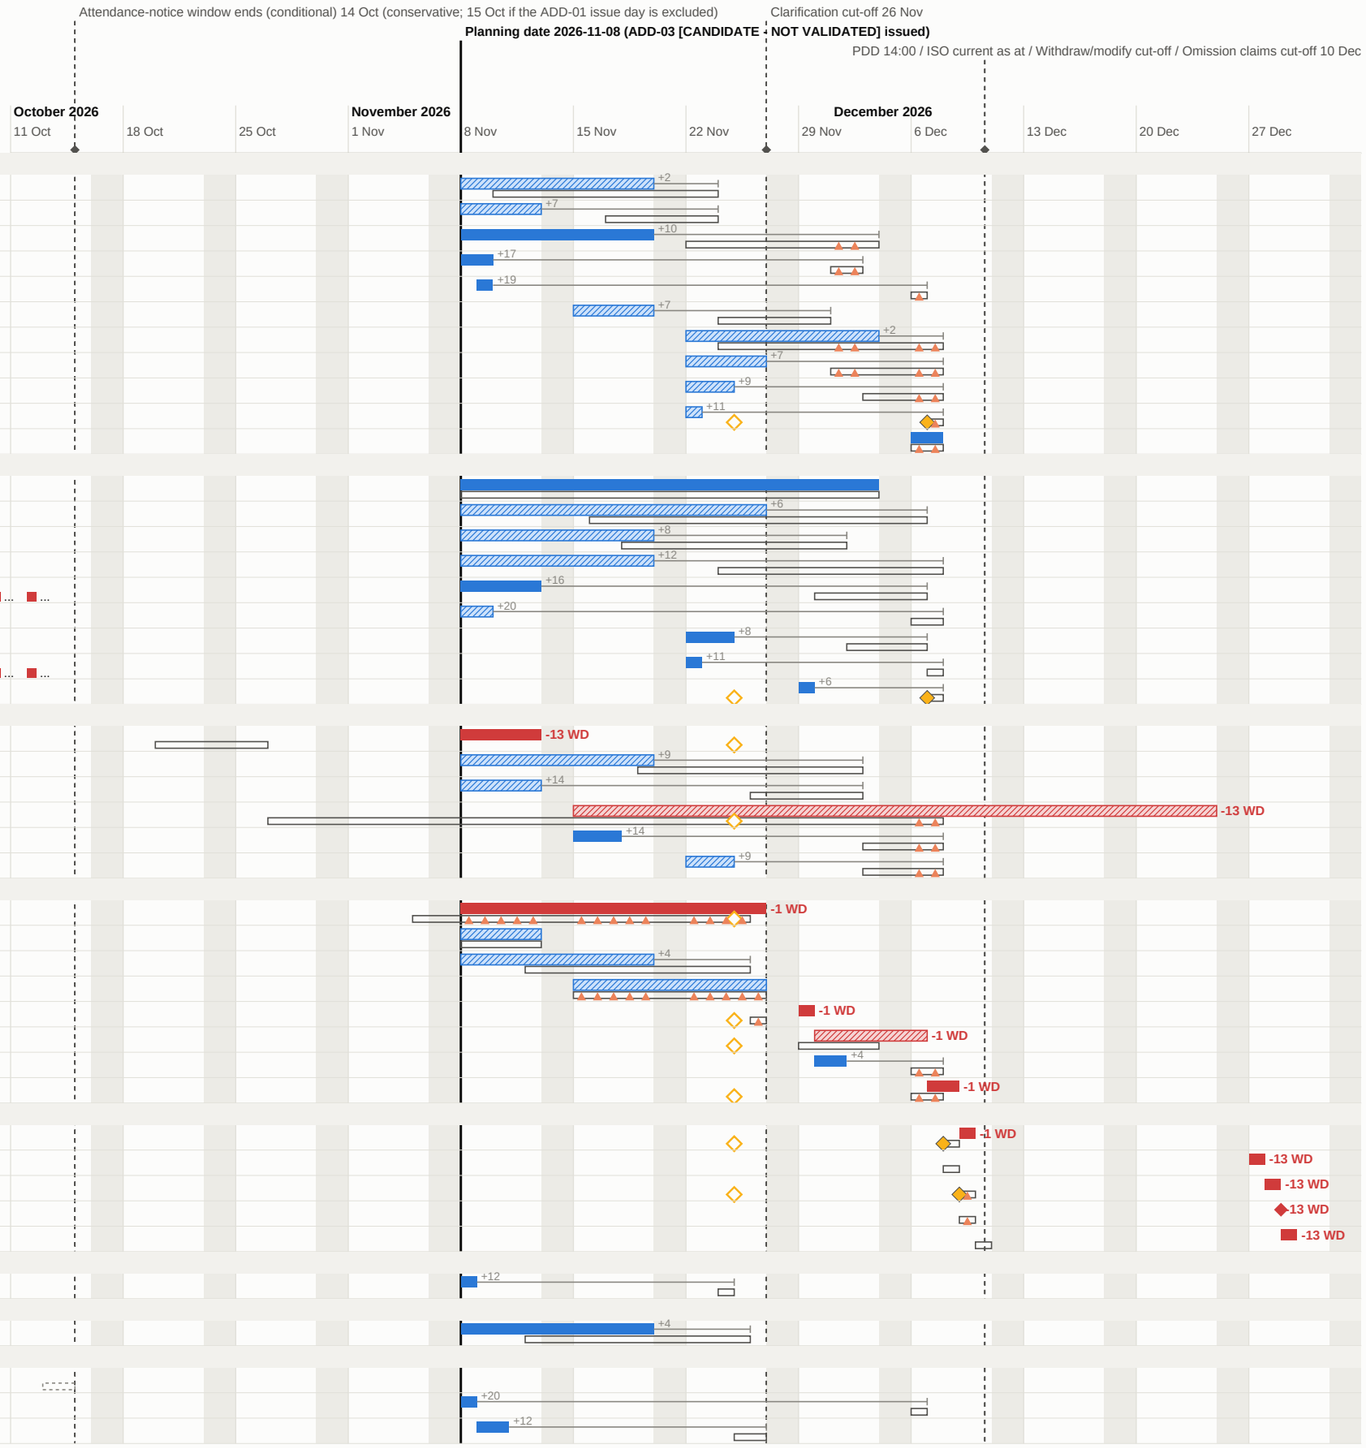

Activity (count) A1 requirement ids	Timing / decision / resource status
Envelope A - Legal (11)	
pcg-wording VOL-I-8.7-01, VOL-IV-F4D-01, VOL-IV-F4D-02, VOL-IV-F4D-03, VOL-IV-F4D-04 +5	
poa-resolutions x3 VOL-I-9.1h-01, VOL-I-9.3-01	
deviations-review VOL-I-9.6-01, VOL-IV-F4E-01, VOL-V-12.1-01, VOL-V-12.2-01, VOL-V-12.3-01 +28	▲ OVERLOAD legal_counsel ■ REVIEW ■ BLOCKED, not supplied: Volume V Schedule 7; the Environmental Permit issued for the site
form-4c-prep VOL-I-8.10-01, VOL-I-8.2-01, VOL-I-9.4-01, VOL-IV-F4C-01, VOL-IV-F4C-02 +4	▲ OVERLOAD legal_counsel
form-4a-prep ADD-01-AppA-01, ADD-03-cover-01, VOL-I-7.1-01, VOL-I-9.3-01, VOL-IV-F4A-01 +1	▲ OVERLOAD legal_counsel
poa x3 VOL-I-9.1h-01, VOL-I-9.3-01	
pcg-execution VOL-I-8.7-01, VOL-IV-F4D-01, VOL-IV-F4D-02, VOL-IV-F4D-03, VOL-IV-F4D-04 +4	▲ OVERLOAD legal_counsel
investment-licence VOL-I-8.9-01	▲ OVERLOAD legal_counsel
form-4c-sign x3 VOL-I-8.10-01, VOL-I-8.2-01, VOL-I-9.4-01, VOL-IV-F4C-01, VOL-IV-F4C-02 +5	▲ OVERLOAD legal_counsel
form-4a ADD-01-AppA-01, ADD-03-cover-01, VOL-I-7.1-01, VOL-I-9.3-01, VOL-IV-F4A-01 +2	◆ GATED I-F4A-FIELDS; ask by 25 Nov; finalise by 7 Dec ▲ OVERLOAD legal_counsel
form-4e VOL-I-9.6-01, VOL-IV-F4E-01, VOL-IV-FORMS-01, VOL-V-12.1-01, VOL-V-12.2-01 +29	◆ 9.6 CHECK: 5 final after start; strict order INFEASIBLE by 15 WD ▲ OVERLOAD ■ BLOCKED: 2 not supplied (row title)
Envelope A - Technical (9)	
technical-proposal ADD-02-5.2-01, ADD-02-T1-1-N3-01, ADD-03-3.2-01, VOL-I-11.3-01, VOL-I-9.2-01 +79	■ REVIEW (confirmed dependency) ■ BLOCKED, not supplied: the Environmental Permit issued for the site ■ REVIEW (proposed relationship)
completion-certs x2 VOL-I-9.5-01	■ REVIEW (proposed relationship)
references x2 VOL-I-8.5-01	■ REVIEW (proposed relationship)
om-evidence VOL-I-8.8-01	
form-4g-review ADD-02-F4G-01, ADD-02-F4G-02, ADD-02-F4G-03, ADD-02-F4G-04, ADD-02-F4G-05 +2	■ REQUIREMENT STALE ■ REQUIREMENT STALE ■ REQUIREMENT STALE ■ REQUIREMENT STALE ■ REQUIREMENT STALE ■ REQUIREMENT STALE ■ ... ■ ...
iso-copy VOL-I-8.3-01	■ REVIEW (proposed relationship)
form-4b-prep x2 VOL-I-9.5-01, VOL-IV-F4B-01	■ REVIEW (proposed relationship)
form-4g-sign ADD-02-F4G-01, ADD-02-F4G-02, ADD-02-F4G-03, ADD-02-F4G-04, ADD-02-F4G-05 +3	■ REQUIREMENT STALE ■ REQUIREMENT STALE ■ REQUIREMENT STALE ■ REQUIREMENT STALE ■ REQUIREMENT STALE ■ REQUIREMENT STALE ■ ... ■ ...
form-4b x2 VOL-I-6.2-02, VOL-I-9.5-01, VOL-IV-F4B-01, VOL-IV-FORMS-01	◆ GATED I-VOL-I-ENV-A-PRICES; ask by 25 Nov; finalise by 7 Dec ■ REVIEW (proposed relationship)
Envelope A - Commercial (6)	
lcc-ratio VOL-I-8.6-01	■ INFEASIBLE by 13 WD ◆ question drafted: ask by 25 Nov
bond-approval VOL-I-6.3-01, VOL-I-6.4-01, VOL-I-6.4-02	■ REVIEW (proposed relationship)
fin-statements x3 VOL-I-8.4-01, VOL-I-8.4-02	
lcc-certificate VOL-I-8.6-01	■ INFEASIBLE by 13 WD ◆ question drafted: ask by 25 Nov ▲ OVERLOAD commercial_manager
fin-standing VOL-I-8.4-01, VOL-I-8.4-02	▲ OVERLOAD commercial_manager
bond-issue VOL-I-6.3-01, VOL-I-6.4-01, VOL-I-6.4-02	▲ OVERLOAD commercial_manager ■ REVIEW (proposed relationship)
Envelope B - Commercial (8)	
fin-model-build ADD-03-Q17-01, VOL-I-10.1-01, VOL-I-10.3-01, VOL-IV-F4F-02	■ INFEASIBLE by 1 WD ◆ question drafted: ask by 25 Nov ▲ OVERLOAD financial_modeller ■ REVIEW (proposed relationship) ■ BLOCKED
model-auditor-appoint VOL-I-10.3-02	
lender-terms VOL-I-10.6-01	
model-audit-review VOL-I-10.3-02	▲ OVERLOAD financial_modeller
fin-model-freeze ADD-03-Q17-01, VOL-I-10.1-01, VOL-I-10.3-01, VOL-IV-F4F-02	■ INFEASIBLE by 1 WD ◆ question drafted: ask by 25 Nov ▲ OVERLOAD financial_modeller ■ BLOCKED
model-audit-opinion VOL-I-10.3-02	■ INFEASIBLE by 1 WD ◆ question drafted: ask by 25 Nov
fin-assumptions VOL-I-10.6-01	▲ OVERLOAD commercial_manager
form-4f ADD-03-Q17-01, VOL-I-10.1-01, VOL-I-10.2-01, VOL-I-10.4-01, VOL-I-10.5-01, VOL-IV-F4F-01 +2	■ INFEASIBLE by 1 WD ◆ question drafted: ask by 25 Nov ▲ OVERLOAD commercial_manager ■ REVIEW (proposed relationship) ■ BLOCKED
Both envelopes - Document control (5)	
assemble-envelope-b VOL-I-10.1-01, VOL-I-6.1-01, VOL-I-6.2-01, VOL-I-App3-01	■ INFEASIBLE by 1 WD ◆ GATED I-VOL-I-ENV-B; ask by 25 Nov; finalise by 8 Dec ■ REVIEW (proposed relationship)
assemble-envelope-a VOL-I-6.1-01, VOL-I-6.2-01, VOL-I-6.2-02, VOL-I-9.1-01, VOL-I-App3-01	■ INFEASIBLE by 13 WD ■ REVIEW (proposed relationship)
copies VOL-I-6.1-01, VOL-I-6.2-01, VOL-I-6.5-01, VOL-I-6.5-02, VOL-I-9.1-01, VOL-I-App3-01	■ INFEASIBLE by 13 WD ◆ GATED I-VOL-I-COPIES; ask by 25 Nov; finalise by 9 Dec ▲ OVERLOAD document_controller ■ REVIEW (proposed relationship)
seal-and-mark VOL-I-6.1-01, VOL-I-6.2-01, VOL-I-9.1-01, VOL-I-App3-01	■ INFEASIBLE by 13 WD ▲ OVERLOAD document_controller ■ REVIEW (proposed relationship)
deliver VOL-I-6.1-01, VOL-I-6.2-01, VOL-I-9.1-01, VOL-I-App3-01	■ INFEASIBLE by 13 WD ■ REVIEW (proposed relationship)
No envelope (actions) - Legal (1)	
consortium-check VOL-I-1.4-01, VOL-I-8.1-01	
No envelope (actions) - Technical (1)	
ground-dd ADD-01-Q4-01, VOL-I-5.5-01	
No envelope (actions) - Bid management (3)	
attendance-notice ADD-01-3.1-01, VOL-I-5.4-01	○ CONDITIONAL: window elapsed, not known if needed
spoc VOL-I-4.3-01	
clarifications VOL-I-3.3-01, VOL-I-3.4-01, VOL-I-4.1-01, VOL-I-5.1-01, VOL-I-5.2-01, VOL-II-4.2-01	

Legend staff effort (early bar ES..EF) · external waiting + staff effort (hatched, ES..EF) · late window LS..LF · float (EF to LF) · 0-WD step · INFEASIBLE: negative float, shortfall in WD (never compressed) · GATED: finalise by (latest start) · ask by: last day to decide whether to raise a clarification request · OPEN DECISION: finalisation needs it by (bar = the activity) · OVERLOAD: role over capacity that day · CONDITIONAL / not scheduled (late window only) · non-working day · planning date · pack milestone

PROPOSAL, not reviewed. Timing, decision readiness and resource feasibility are separate statuses; resource levelling is NOT implemented; overloads are reported, not resolved. No bidder references, certificates, attendance or financial standing are assumed to exist.
Each row: activity id, count, then the A1 requirement ids that fit (+n more); ALL ids are in the row's hover title, gantt.html and programme.csv. Load window: late (LS..LF, clipped at the planning date).
Milestones outside the chart: Reference look-back start 2016-12-11 (conservative; 2016-12-10 if the boundary day counts); Blackout start 2026-09-14; Pre-Bid Conference 10:00 2026-09-30; Site visit (optional) 2026-10-01; Proposal validity end 2027-05-09 (conservative; 2027-05-08 if the PDD counts as day 1); Bid bond validity end 2027-07-08 (conservative; 2027-07-07 if the PDD counts as day 1).
REVIEW (<status> ...) tags: Relationship status: confirmed = stated in the documents (the entry quotes the cross-reference), not confirmed by a person; proposed = inferred by a curator or a model, a person decides; possible = a weaker inference.
form-4e: VOL-I 9.6 CHECK (Form 4-E against the whole Proposal; form_4e_checks.csv): form-4a, form-4b, lcc-certificate, form-4f, model-audit-opinion final after Form 4-E starts on 2026-12-06; a strict order (Form 4-E after every Proposal document) INFEASIBLE by 15 WD on the assumed durations; 13 WD of it existed before the ordering (assemble-envelope-a, copies, deliver, fin-model-build, fin-model-freeze, form-4f, lcc-certificate, lcc-ratio, model-audit-opinion, seal-and-mark already late); the ordering itself adds 2 WD and makes late form-4e, model-audit-review, model-auditor-appoint; how Form 4-E is cross-checked against the documents final after it starts: decision recorded on I-FORM-4E-CROSS-CHECK; whether and how Form 4-E can list a qualification of a commercial term without commercial information (VOL-I 9.6, 6.2, 10.5): decision recorded on I-FORM-4E-COMMERCIAL-QUALIFICATION; no duration, setting or dependency was changed
