


A5 bid programme - Gantt - ADD-02 - planning date 2026-10-22 (PROPOSAL, not reviewed)

Earliest dates: forward pass from 2026-10-22 (first Working Day on or after the planning date, the ADD-02 issue date). Latest dates: backward pass from the pack deadlines. Working Days Sun-Thu (VOL-1 2.4). Every duration, effort, waiting party and capacity is a PROVISIONAL ASSUMPTION (config/assumptions.yaml).

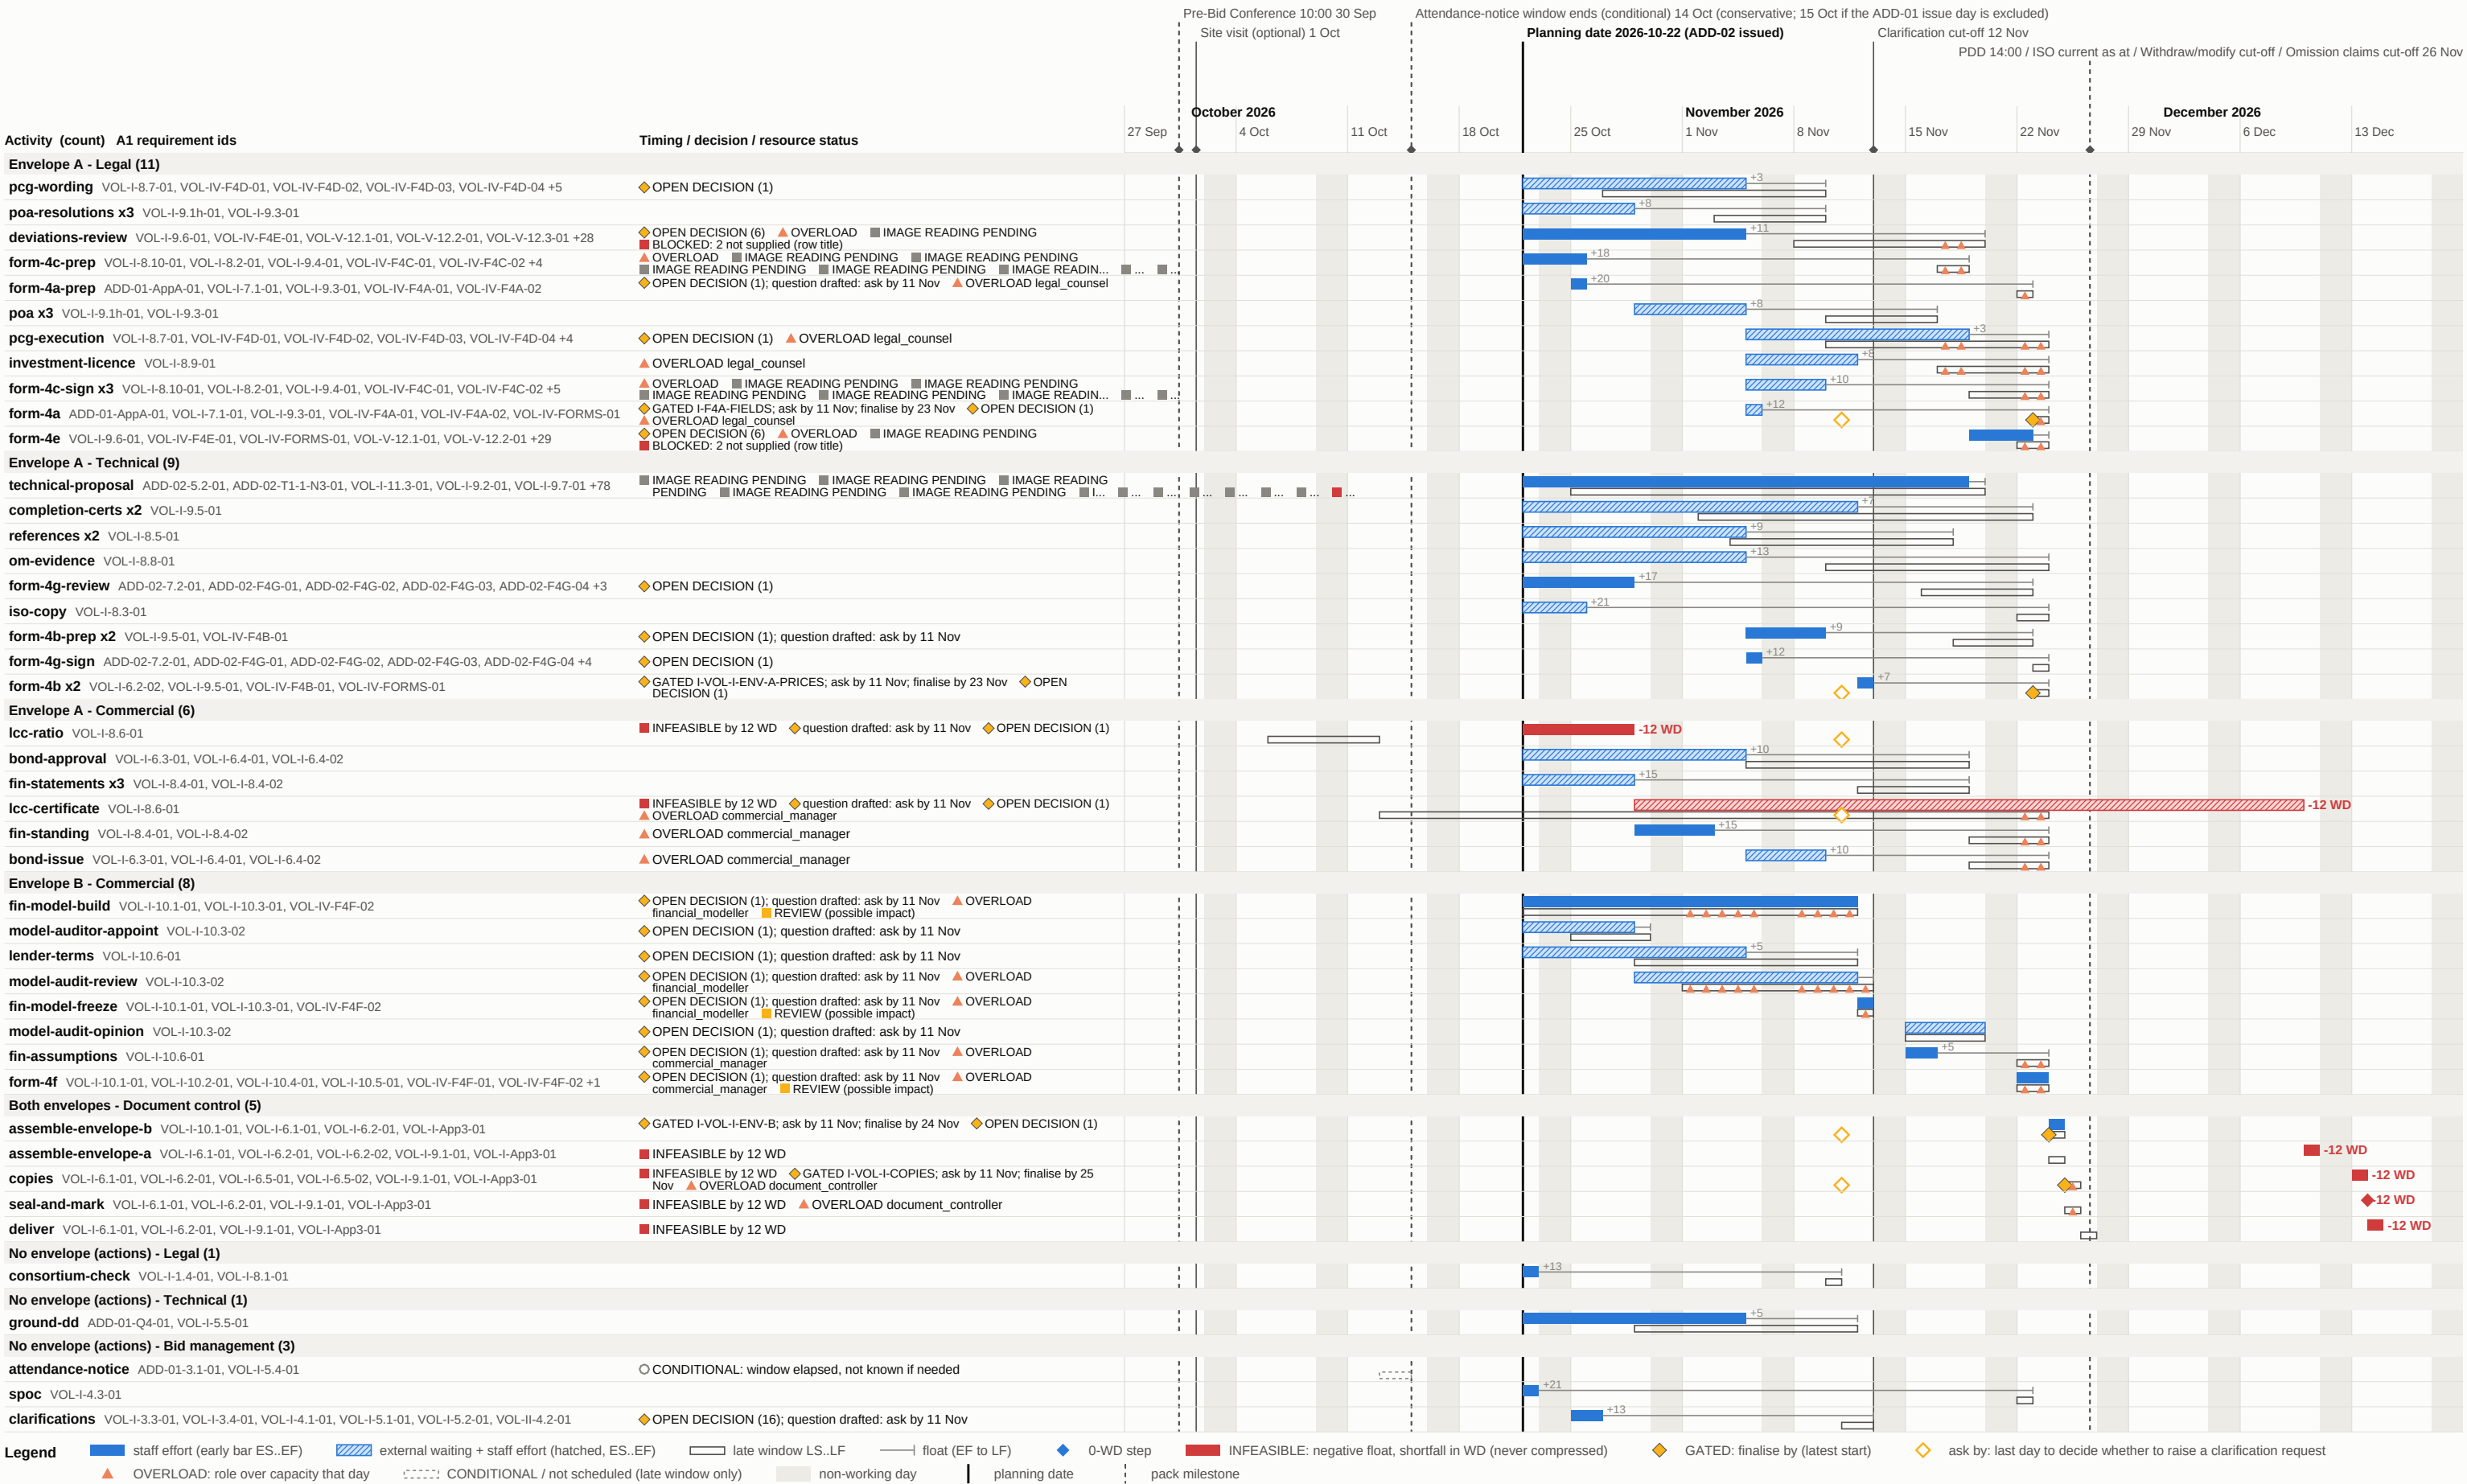

PROPOSAL, not reviewed. Timing, decision readiness and resource feasibility are separate statuses; resource levelling is NOT implemented; overloads are reported, not resolved. No bidder references, certificates, attendance or financial standing are assumed to exist.

Each row: activity id, count, then the A1 requirement ids that fit (+n more); ALL ids are in the row's hover title, [ganttt.html](#) and [programme.csv](#). Load window: late (LS..LF, clipped at the planning date).

Milestones outside the chart: Reference look-back start 2016-11-27 (conservative; 2016-11-26 if the boundary day counts); Blackout start 2026-09-14; Proposal validity end 2027-04-25 (conservative; 2027-04-24 if the PDD counts as day 1); Bid bond validity end 2027-05-25 (conservative; 2027-05-24 if the PDD counts as day 1).

REVIEW (<status> ...) tags: Relationship status: confirmed = stated in the documents (the entry quotes the cross-reference), not confirmed by a person; proposed = inferred by a curator or a model, a person decides; possible = a weaker inference.

OPEN DECISION (n) tags: open issues of the rows an activity's own work rests on, a person's decision with none recorded (HUMAN DECISION PENDING; also in the Flags column, programme.csv and README); clarifications lists all 16. On lcc-ratio, lcc-certificate: I-LCC-ISSUER (LCC issuer and lead time not stated). On fin-model-build, model-auditor-appoint, lender-terms, model-audit-review +5: I-VOL-I-ENV-B (Envelope B: auditor opinion and financing schedule vs VOL-I 10.1 'only'). On technical-proposal, deviations-review, form-4e: I-PERMIT (Environmental Permit not supplied; Permit compliance not claimed); I-CONCESSION (term from PCOD (VOL-I 12.1) or Effective Date (VOL-V 3.1)? ADD-Q2 Q7 cites VOL-I 3.2 only); I-VOL-II-T24-TENSIONS (Table 2-4 'all values are maxima' vs the chlorine and pH ranges);

I- FLOWS (dry weather flow undefined; Q11: design to the Volume II figures). On technical-proposal: I-VOL-I-PAGE-LIMIT-Q2 (page limit: whether ADD-01 Q2 (narrative only) still holds after ADD-02 2.1 (150 pages)); I-VOL-II-AT-ALL-TIMES ('at all times' (VOL-II 2.4) with each parameter's printed basis: proposed reading, not decided); I-VOL-II-COMPLIANCE-POINT (Table 2-4 compliance point: 'Point of Discharge', 'at outlet' or the delivery point (Drawing 03-C-114)?). On pcg-wording, pcg-execution: I-F4D-WORDING (Form 4-D: how far its wording may change (VOL-I 8.7)). On deviations-review, form-4e: I-VOL-V-MISSING (VOL-V extract: Schedules 7, 9, 11, 12 and Direct Agreement missing); I-VOL-V-PERSISTENT-BREACH ('second occurrence' of a persistent breach undefined). On form-4a-prep, form-4a: I-F4A-FIELDS

(reissued Form 4-A: stale printed PDD, dropped fields, correction method). On form-4g-review, form-4g-sign: I-F4G-NO (Form 4-G: effect of a 'No' answer). On form-4b-prep, form-4b: I-VOL-I-ENV-A-PRICES (Form 4-B contract values vs no commercial information in Envelope A). On form-4c-prep, form-4c-sign: I-F4C-EXCLUSION (Form 4-C: 'exclusion' category).
